AOU
الجامعة العربية المفتوحة
Arab Open University
Faculty of Computer Studies

T227

Change, Strategy and Projects at Work

AOU EGYPT

Final Examination
Spring Semester 2025/2026

Date: 13/ June /2026

Number of Exam Pages: 5 (including this cover sheet)	**Time Allowed:** 3 Hours

Instructions:

- Total Marks: **100 marks**
- This exam consists of **3** parts.
- **ALL questions** must be answered in the External Answer booklet.
- Be sure you write your **name and ID** on the External Answer booklet.
- **Calculators** are allowed.

Part 1: MULTIPLE CHOICE QUESTIONS. Answer all questions by selecting the appropriate choice. Each question is worth 2 marks for a total of 20 marks.

1. Project implementation commences when:
    a. the project sponsor approves the final report
    b. all plans are finally authorized at the date specified in the project schedule
    c. the project team completes the first milestone
    d. the customer accepts the final deliverable
2. A start-up meeting can fulfill the purpose of:
    a. closing all procurement contracts
    b. presenting or reiterating the project vision and motivating the project stakeholders
    c. archiving project data and records
    d. conducting the final project evaluation
3. The key things to be planned, monitored, and controlled are:
    a. leadership, motivation, and communication
    b. time, cost, and specifications
    c. scope, risk, and procurement only
    d. quality, staffing, and closure
4. In a closed loop system:
    a. project reports are written only at closure
    b. revised plans and schedules should follow corrective actions
    c. project stakeholders are excluded from feedback
    d. the project schedule cannot be changed
5. Earned Value Management recognizes that it is necessary to jointly consider:
    a. leadership, conflict, and motivation
    b. stakeholder satisfaction, project reports, and closure
    c. time, cost, and project performance
    d. budget, documentation, and archiving
6. Project managers perform both:
    a. functional and technical duties
    b. process and people functions
    c. administrative and legal functions
    d. financial and operational functions
7. Process functions fall into the following groups:
    a. leadership, teambuilding, motivation, communication, and time management
    b. initiating, planning, executing, monitoring and controlling, and closing out projects
    c. credibility, sensitivity, leadership, and conflict management
    d. conservation of resources, reporting, and risk protection
8. Functional managers are usually:
    a. generalists that can oversee many functional areas
    b. specialists, analytically oriented, and know the details of each operation
    c. facilitators responsible for project integration
    d. responsible for organizing, staffing, budgeting, and directing projects

ADEPT

9. Project termination consists of:
    a. all activities consistent with closing out the project
    b. only the final payment to the contractor
    c. only the transfer of staff to another project
    d. all activities related to starting a new project
10. At project closure, the following actions, as a minimum, need to be taken:
    a. project initiation, project planning, and project execution
    b. project vision, project objectives, and stakeholder motivation
    c. orderly and secure archival of project data, project report, and project evaluation/debriefing meeting
    d. cost variance analysis, schedule variance analysis, and budget approval

Part 2: Long and Short ESSAY QUESTIONS. Answer all the questions in this part. Total marks are 20 marks.

Question 1: Project Manager Roles and Responsibilities [10 marks]
The project manager has many roles and responsibilities during the project.

a. Explain the difference between a functional manager and a project manager. **[4 marks]**
b. List three process functions performed by project managers. **[3 marks]**
c. List three people functions performed by project managers. **[3 marks]**

Question 2: Project Closure and Learning [10 marks]
Project closure helps the organization learn from completed projects.

a. Define project termination. **[2 marks]**
b. Mention three actions that should be taken at project closure. **[3 marks]**
c. Explain why project information and experiences should be recorded. **[5 marks]**

Part 3: Practical QUESTIONS. Answer all the questions in this part. Total marks are 60 marks.


Question 3: [20 marks]
You are managing a software development project with the following activities:

a. Draw the project network diagram **(10 Marks)**
b. Determine the critical path and total project duration. **(5 Marks)**
c. Calculate the float (slack) for each activity. **(5 Marks)**

Tasks	Predecessor	Duration	Slack
A	-	4	
B	A	6	
C	A	5	
D	B	7	
E	C	8	
F	C	4	
G	D,E	5	
H	F,G	6	
I	H	3	

ROUGH COPY

Question 4: [31.5 marks]

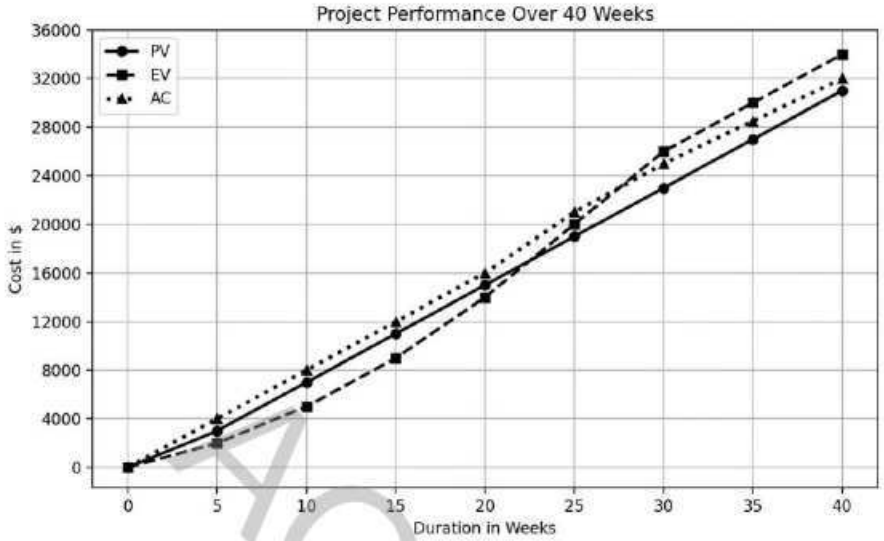

Refer to the graph below, which displays the Planned Value (PV), Earned Value (EV), and Actual Cost (AC) over a 40-week project timeline.

a. Estimate the values of PV, EV, and AC at the following time intervals from the graph: **[13.5 marks]**

Week	PV	AC	EV
Week0			
Week 5			
Week 10			
Week 15			
Week 20			
Week 25			
Week 30			
Week 35			
Week 40			

b. Calculate the following values for each selected week and fill the table. **[18 marks]**

Note: Analyze the project performance based on the values obtained: project behind schedule? ahead of schedule? over budget? under budget?

Week	SV	CV	Analyze
Week 0			
Week 5			
Week 10			
Week 15			
Week 20			
Week 25			
Week 30			
Week 35			
Week 40			


AOU EGYPT

Question 4: [8.5 marks]


a) Explain the Forcefield analysis technique. [5 Marks]

b) Consider the following two projects :

Project 1



Project 2



1) Calculate the overall probability of achieving project 1? [1 Marks]

2) Calculate the overall probability of achieving project 2? [1 Marks]

3) Which project is better to be developed between Project 1 and Project 2, and why? [1.5 Marks]

End of questions

AQU EGYPT
